

WATERS (SURFACE WATER BASINS)

ID	Task Name	Duration	Start	Finish	% Complete	Predk	2003				2004				2005				2006				2007				2008							
							Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1							
1	Sandia SWB	27.88 days	Mon 8/25/03	Thu 10/2/03	100%																													
2	Organizational Meetings	5 days	Mon 8/25/03	Fri 8/29/03	100%																													
3	Preparation of Project Plan	20 days	Tue 9/2/03	Mon 9/29/03	100%	2																												
4	Sort and Compare	6 hrs	Tue 9/30/03	Tue 9/30/03	100%	3																												
5	Abstract File	13 hrs	Tue 9/30/03	Thu 10/2/03	100%	4																												
6	QA and Archive	4 hrs	Thu 10/2/03	Thu 10/2/03	100%	5																												
7	Upper Rio Grande SWB	158.63 days	Mon 2/17/03	Tue 9/30/03	30%																													
8	Organizational Meetings	5 days	Mon 2/17/03	Fri 2/21/03	100%																													
9	Preparation of Project Plan	20 days	Mon 2/24/03	Fri 3/21/03	100%	8																												
10	Sort and Compare	132 hrs	Mon 3/24/03	Tue 4/15/03	100%	9																												
11	Abstract File	273 hrs	Tue 4/15/03	Tue 6/3/03	18%	10																												
12	QA and Archive	83 days	Tue 6/3/03	Tue 9/30/03	0%	11																												
13	San Juan SWB	50.13 days	Mon 8/25/03	Wed 11/5/03	0%																													
14	Organizational Meetings	5 days	Mon 8/25/03	Fri 8/29/03	0%																													
15	Preparation of Project Plan	20 days	Tue 9/2/03	Mon 9/29/03	0%	14																												
16	Sort and Compare	54 hrs	Tue 9/30/03	Wed 10/8/03	0%	15																												
17	Abstract File	113 hrs	Wed 10/8/03	Wed 10/29/03	0%	16																												
18	QA and Archive	34 hrs	Wed 10/29/03	Wed 11/5/03	0%	17																												
19	Viriden Valley SWB	31.38 days	Tue 9/2/03	Thu 10/16/03	50%																													
20	Organizational Meetings	5 days	Tue 9/2/03	Mon 9/8/03	100%																													
21	Preparation of Project Plan	20 days	Tue 9/9/03	Mon 10/6/03	53%	20																												
22	Sort and Compare	14 hrs	Tue 10/7/03	Wed 10/8/03	0%	21																												
23	Abstract File	28 hrs	Wed 10/8/03	Wed 10/15/03	0%	22																												
24	QA and Archive	9 hrs	Wed 10/15/03	Thu 10/16/03	0%	23																												
25	Upper Pecos SWB	34.25 days	Mon 9/29/03	Tue 11/18/03	20%																													
26	Organizational Meetings	5 days	Mon 9/29/03	Fri 10/3/03	100%																													
27	Preparation of Project Plan	20 days	Mon 10/6/03	Mon 11/3/03	9%	26																												
28	Sort and Compare	20 hrs	Tue 11/4/03	Thu 11/6/03	0%	27																												
29	Abstract File	41 hrs	Thu 11/6/03	Fri 11/14/03	0%	28																												
30	QA and Archive	13 hrs	Fri 11/14/03	Tue 11/18/03	0%	29																												
31	Lower Rio Grande SWB (FIX)	25.38 days	Tue 11/18/03	Fri 12/26/03	0%	30																												
32	Organizational Meetings	5 days	Tue 11/18/03	Tue 11/25/03	0%																													
33	Preparation of Project Plan	20 days	Tue 11/25/03	Fri 12/26/03	0%	32																												
34	Sort and Compare	1 hr	Fri 12/26/03	Fri 12/26/03	0%	33																												
35	Abstract File	1 hr	Fri 12/26/03	Fri 12/26/03	0%	34																												
36	QA and Archive	1 hr	Fri 12/26/03	Fri 12/26/03	0%	35																												
37	Bluewater SWB	27 days	Fri 12/26/03	Tue 2/3/04	0%	36																												
38	Organizational Meetings	5 days	Fri 12/26/03	Fri 1/2/04	0%																													
39	Preparation of Project Plan	20 days	Fri 1/2/04	Fri 1/30/04	0%	38																												
40	Sort and Compare	4 hrs	Fri 1/30/04	Mon 2/2/04	0%	39																												
41	Abstract File	9 hrs	Mon 2/2/04	Tue 2/3/04	0%	40																												
42	QA and Archive	3 hrs	Tue 2/3/04	Tue 2/3/04	0%	41																												

Project: WATERS
Date: Fri 11/14/03

Task: Milestone: Rolled Up Task: Rolled Up Progress: External Tasks: Group By Summary:

Progress: Summary: Rolled Up Milestone: Split: Project Summary:


WATERS (SURFACE WATER BASINS)

ID	Task Name	Duration	Start	Finish	% Complete	Predt	2003				2004				2005				2006				2007				2008							
							Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1							
43	Estancia SWB	29.25 days	Tue 2/3/04	Mon 3/15/04	0%	42	<div style="display: flex; justify-content: space-between;"> Estancia SWB 3/15/2004 </div>																											
44	Organizational Meetings	5 days	Tue 2/3/04	Tue 2/10/04	0%		<div style="display: flex; justify-content: space-between;"> Organizational Meetings </div>																											
45	Preparation of Project Plan	20 days	Tue 2/10/04	Tue 3/9/04	0%	44	<div style="display: flex; justify-content: space-between;"> Preparation of Project Plan </div>																											
46	Sort and Compare	9 hrs	Tue 3/9/04	Wed 3/10/04	0%	45	<div style="display: flex; justify-content: space-between;"> Sort and Compare </div>																											
47	Abstract File	19 hrs	Wed 3/10/04	Mon 3/15/04	0%	46	<div style="display: flex; justify-content: space-between;"> Abstract File </div>																											
48	QA and Archive	6 hrs	Mon 3/15/04	Mon 3/15/04	0%	47	<div style="display: flex; justify-content: space-between;"> QA and Archive </div>																											
49	Canadian River & Dry Cimmaron SW	51.5 days	Mon 3/15/04	Wed 5/26/04	0%	48	<div style="display: flex; justify-content: space-between;"> Canadian River & Dry Cimmaron SWB 5/26/2004 </div>																											
50	Organizational Meetings	5 days	Mon 3/15/04	Mon 3/22/04	0%		<div style="display: flex; justify-content: space-between;"> Organizational Meetings </div>																											
51	Preparation of Project Plan	20 days	Mon 3/22/04	Mon 4/19/04	0%	50	<div style="display: flex; justify-content: space-between;"> Preparation of Project Plan </div>																											
52	Sort and Compare	57 hrs	Mon 4/19/04	Wed 4/28/04	0%	51	<div style="display: flex; justify-content: space-between;"> Sort and Compare </div>																											
53	Abstract File	119 hrs	Thu 4/29/04	Wed 5/19/04	0%	52	<div style="display: flex; justify-content: space-between;"> Abstract File </div>																											
54	QA and Archive	36 hrs	Wed 5/19/04	Wed 5/26/04	0%	53	<div style="display: flex; justify-content: space-between;"> QA and Archive </div>																											
55	Gila - San Francisco SWB	33.38 days	Wed 5/26/04	Mon 7/12/04	0%	54	<div style="display: flex; justify-content: space-between;"> Gila - San Francisco SWB 7/12/2004 </div>																											
56	Organizational Meetings	5 days	Wed 5/26/04	Wed 6/2/04	0%		<div style="display: flex; justify-content: space-between;"> Organizational Meetings </div>																											
57	Preparation of Project Plan	20 days	Wed 6/2/04	Wed 6/30/04	0%	56	<div style="display: flex; justify-content: space-between;"> Preparation of Project Plan </div>																											
58	Sort and Compare	18 hrs	Wed 6/30/04	Fri 7/2/04	0%	57	<div style="display: flex; justify-content: space-between;"> Sort and Compare </div>																											
59	Abstract File	38 hrs	Fri 7/2/04	Fri 7/9/04	0%	58	<div style="display: flex; justify-content: space-between;"> Abstract File </div>																											
60	QA and Archive	11 hrs	Fri 7/9/04	Mon 7/12/04	0%	59	<div style="display: flex; justify-content: space-between;"> QA and Archive </div>																											
61	Hot Springs SWB	25.88 days	Mon 7/12/04	Tue 8/17/04	0%	60	<div style="display: flex; justify-content: space-between;"> Hot Springs SWB 8/17/2004 </div>																											
62	Organizational Meetings	5 days	Mon 7/12/04	Mon 7/19/04	0%		<div style="display: flex; justify-content: space-between;"> Organizational Meetings </div>																											
63	Preparation of Project Plan	20 days	Mon 7/19/04	Mon 8/16/04	0%	62	<div style="display: flex; justify-content: space-between;"> Preparation of Project Plan </div>																											
64	Sort and Compare	2 hrs	Mon 8/16/04	Mon 8/16/04	0%	63	<div style="display: flex; justify-content: space-between;"> Sort and Compare </div>																											
65	Abstract File	4 hrs	Tue 8/17/04	Tue 8/17/04	0%	64	<div style="display: flex; justify-content: space-between;"> Abstract File </div>																											
66	QA and Archive	1 hr	Tue 8/17/04	Tue 8/17/04	0%	65	<div style="display: flex; justify-content: space-between;"> QA and Archive </div>																											
67	Hueco SWB	27.25 days	Tue 8/17/04	Thu 9/23/04	0%	66	<div style="display: flex; justify-content: space-between;"> Hueco SWB 9/23/2004 </div>																											
68	Organizational Meetings	5 days	Tue 8/17/04	Tue 8/24/04	0%		<div style="display: flex; justify-content: space-between;"> Organizational Meetings </div>																											
69	Preparation of Project Plan	20 days	Tue 8/24/04	Tue 9/21/04	0%	68	<div style="display: flex; justify-content: space-between;"> Preparation of Project Plan </div>																											
70	Sort and Compare	5 hrs	Tue 9/21/04	Wed 9/22/04	0%	69	<div style="display: flex; justify-content: space-between;"> Sort and Compare </div>																											
71	Abstract File	10 hrs	Wed 9/22/04	Thu 9/23/04	0%	70	<div style="display: flex; justify-content: space-between;"> Abstract File </div>																											
72	QA and Archive	3 hrs	Thu 9/23/04	Thu 9/23/04	0%	71	<div style="display: flex; justify-content: space-between;"> QA and Archive </div>																											
73	Gallup SWB	33.38 days	Thu 9/23/04	Wed 11/10/04	0%	72	<div style="display: flex; justify-content: space-between;"> Gallup SWB 11/10/2004 </div>																											
74	Organizational Meetings	5 days	Thu 9/23/04	Thu 9/30/04	0%		<div style="display: flex; justify-content: space-between;"> Organizational Meetings </div>																											
75	Preparation of Project Plan	20 days	Thu 9/30/04	Thu 10/28/04	0%	74	<div style="display: flex; justify-content: space-between;"> Preparation of Project Plan </div>																											
76	Sort and Compare	18 hrs	Thu 10/28/04	Tue 11/2/04	0%	75	<div style="display: flex; justify-content: space-between;"> Sort and Compare </div>																											
77	Abstract File	38 hrs	Tue 11/2/04	Mon 11/8/04	0%	76	<div style="display: flex; justify-content: space-between;"> Abstract File </div>																											
78	QA and Archive	11 hrs	Mon 11/8/04	Wed 11/10/04	0%	77	<div style="display: flex; justify-content: space-between;"> QA and Archive </div>																											
79	Roswell Artesian SWB	61.63 days	Wed 11/10/04	Thu 2/3/05	0%	78	<div style="display: flex; justify-content: space-between;"> Roswell Artesian SWB 2/3/2005 </div>																											
80	Organizational Meetings	5 days	Wed 11/10/04	Wed 11/17/04	0%		<div style="display: flex; justify-content: space-between;"> Organizational Meetings </div>																											
81	Preparation of Project Plan	20 days	Wed 11/17/04	Wed 12/15/04	0%	80	<div style="display: flex; justify-content: space-between;"> Preparation of Project Plan </div>																											
82	Sort and Compare	79 hrs	Wed 12/15/04	Wed 12/29/04	0%	81	<div style="display: flex; justify-content: space-between;"> Sort and Compare </div>																											
83	Abstract File	164 hrs	Wed 12/29/04	Wed 1/26/05	0%	82	<div style="display: flex; justify-content: space-between;"> Abstract File </div>																											
84	QA and Archive	50 hrs	Wed 1/26/05	Thu 2/3/05	0%	83	<div style="display: flex; justify-content: space-between;"> QA and Archive </div>																											

Project: WATERS Date: Fri 11/14/03	Task	Milestone	Rolled Up Task	Rolled Up Progress	External Tasks	Group By Summary
	Progress	Summary	Rolled Up Milestone	Split	Project Summary	

WATERS (SURFACE WATER BASINS)

ID	Task Name	Duration	Start	Finish	% Complete	Predt	2003				2004				2005				2006				2007				2008						
							Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1						
85	Carlsbad SWB	46 days	Thu 2/3/05	Fri 4/8/05	0%	84									Carlsbad SWB	4/8/2005																	
86	Organizational Meetings	5 days	Thu 2/3/05	Thu 2/10/05	0%																												
87	Preparation of Project Plan	20 days	Thu 2/10/05	Thu 3/10/05	0%	86																											
88	Sort and Compare	45 hrs	Thu 3/10/05	Fri 3/18/05	0%	87																											
89	Abstract File	94 hrs	Fri 3/18/05	Tue 4/5/05	0%	88																											
90	QA and Archive	29 hrs	Tue 4/5/05	Fri 4/8/05	0%	89																											
91	Hondo SWB	27.13 days	Fri 4/8/05	Tue 5/17/05	0%	90									Hondo SWB	5/17/2005																	
92	Organizational Meetings	5 days	Fri 4/8/05	Fri 4/15/05	0%																												
93	Preparation of Project Plan	20 days	Fri 4/15/05	Fri 5/13/05	0%	92																											
94	Sort and Compare	5 hrs	Fri 5/13/05	Mon 5/16/05	0%	93																											
95	Abstract File	9 hrs	Mon 5/16/05	Tue 5/17/05	0%	94																											
96	QA and Archive	3 hrs	Tue 5/17/05	Tue 5/17/05	0%	95																											
97	Penasco SWB	26.38 days	Wed 5/18/05	Thu 6/23/05	0%	96									Penasco SWB	6/23/2005																	
98	Organizational Meetings	5 days	Wed 5/18/05	Tue 5/24/05	0%																												
99	Preparation of Project Plan	20 days	Wed 5/25/05	Tue 6/21/05	0%	98																											
100	Sort and Compare	3 hrs	Wed 6/22/05	Wed 6/22/05	0%	99																											
101	Abstract File	6 hrs	Wed 6/22/05	Thu 6/23/05	0%	100																											
102	QA and Archive	2 hrs	Thu 6/23/05	Thu 6/23/05	0%	101																											
103	Fort Sumner SWB	50.13 days	Thu 6/23/05	Thu 9/1/05	0%	102									Fort Sumner SWB	9/1/2005																	
104	Organizational Meetings	5 days	Thu 6/23/05	Thu 6/30/05	0%																												
105	Preparation of Project Plan	20 days	Thu 6/30/05	Thu 7/28/05	0%	104																											
106	Sort and Compare	54 hrs	Thu 7/28/05	Mon 8/8/05	0%	105																											
107	Abstract File	113 hrs	Mon 8/8/05	Fri 8/26/05	0%	106																											
108	QA and Archive	34 hrs	Fri 8/26/05	Thu 9/1/05	0%	107																											
109	Hagerman Canal SWB	25.88 days	Thu 9/1/05	Fri 10/7/05	0%	108									Hagerman Canal SWB	10/7/2005																	
110	Organizational Meetings	5 days	Thu 9/1/05	Thu 9/8/05	0%																												
111	Preparation of Project Plan	20 days	Thu 9/8/05	Thu 10/6/05	0%	110																											
112	Sort and Compare	2 hrs	Thu 10/6/05	Thu 10/6/05	0%	111																											
113	Abstract File	4 hrs	Thu 10/6/05	Fri 10/7/05	0%	112																											
114	QA and Archive	1 hr	Fri 10/7/05	Fri 10/7/05	0%	113																											
115	Jal SWB	25.38 days	Fri 10/7/05	Fri 11/11/05	0%	114									Jal SWB	11/11/2005																	
116	Organizational Meetings	5 days	Fri 10/7/05	Fri 10/14/05	0%																												
117	Preparation of Project Plan	20 days	Fri 10/14/05	Fri 11/11/05	0%	116																											
118	Sort and Compare	1 hr	Fri 11/11/05	Fri 11/11/05	0%	117																											
119	Abstract File	1 hr	Fri 11/11/05	Fri 11/11/05	0%	118																											
120	QA and Archive	1 hr	Fri 11/11/05	Fri 11/11/05	0%	119																											
121	Middle Rio Grande SWB	165.63 days	Fri 11/11/05	Mon 7/3/06	0%	120									Middle Rio Grande SWB	7/3/2006																	
122	Organizational Meetings	5 days	Fri 11/11/05	Fri 11/18/05	0%																												
123	Preparation of Project Plan	20 days	Fri 11/18/05	Fri 12/16/05	0%	122																											
124	Sort and Compare	304 hrs	Fri 12/16/05	Wed 2/8/06	0%	123																											
125	Abstract File	630 hrs	Wed 2/8/06	Tue 5/30/06	0%	124																											
126	QA and Archive	191 hrs	Tue 5/30/06	Mon 7/3/06	0%	125																											

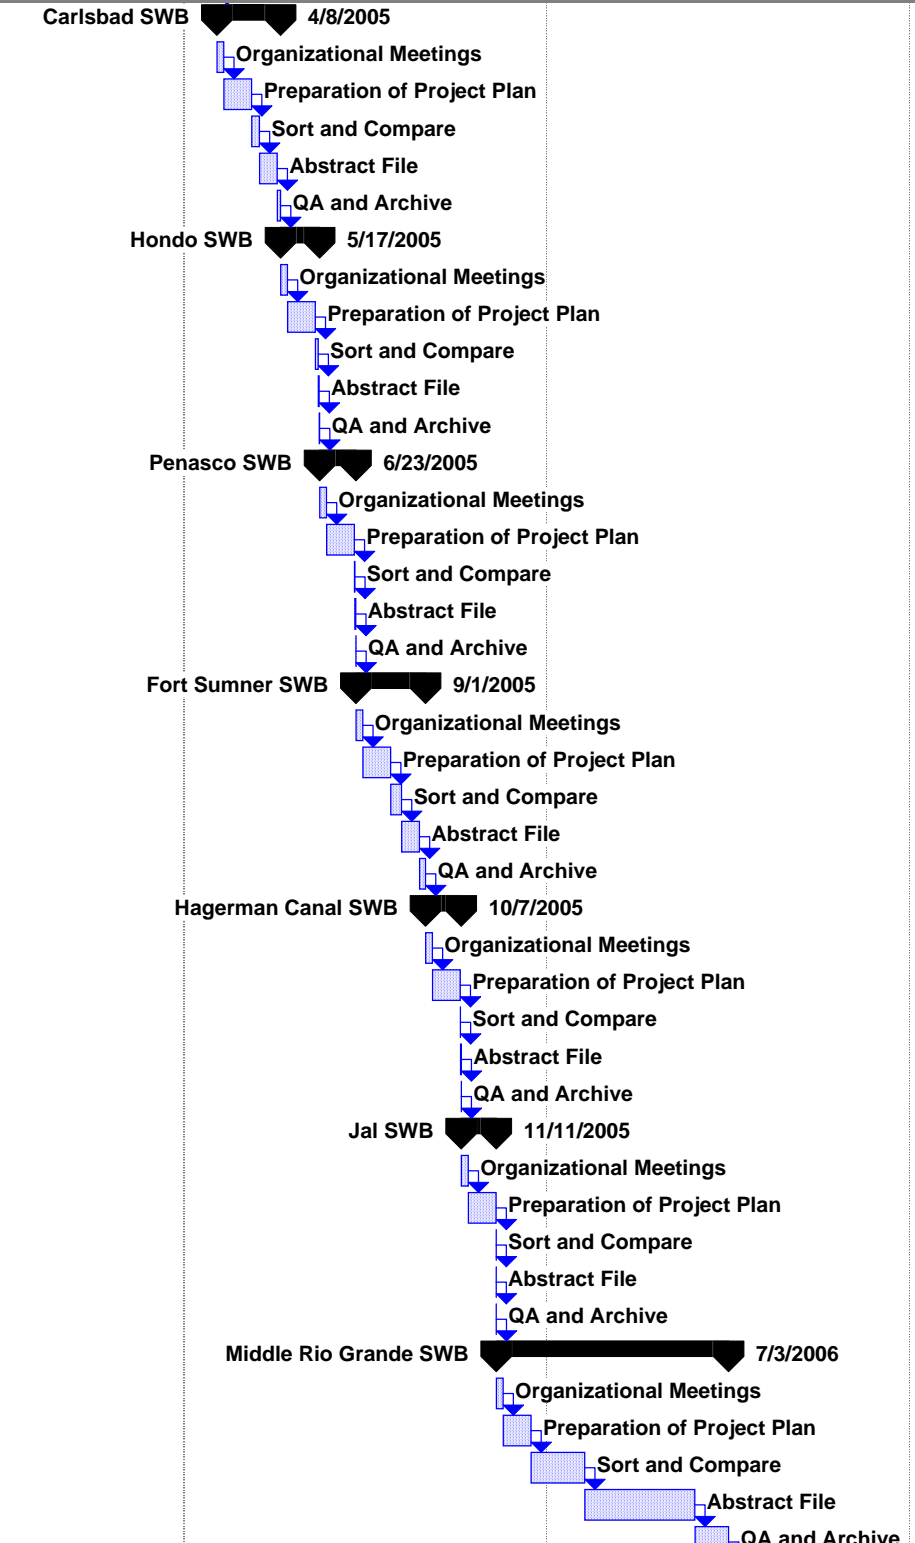

Project: WATERS
Date: Fri 11/14/03

Task: Milestone: Rolled Up Task: Rolled Up Progress: External Tasks: Group By Summary:

Progress: Summary: Rolled Up Milestone: Split: Project Summary:

